

### **07/01/23**

- The Organ disassembly is complete.
- We are continuing to clean the structure. We are now working on the 3<sup>rd</sup> deck
- We have begun to build additional scaffolding over where the organ was to access the ceiling and high walls for cleaning.

### **07/03/23**

- Continue cleaning the structure.
- Complete additional scaffolding over original organ location.

In addition to the Rebuild Holy Cross team coming together this week, various team members met with representatives to gather information and pricing to replace the organ and stained-glass windows. Pictures (pre-fire) were sent to companies who will visit in July to offer options for paint and design.










Please see attached Project Manager Log for 06/28/23.

**06/28/23**


- The Organ disassembly is about 90% complete.
- We are continuing to clean the ceiling working from the alter towards the front of the church.

**06/29/23**

- Continue the organ disassembly.
- Continue cleaning the structure.

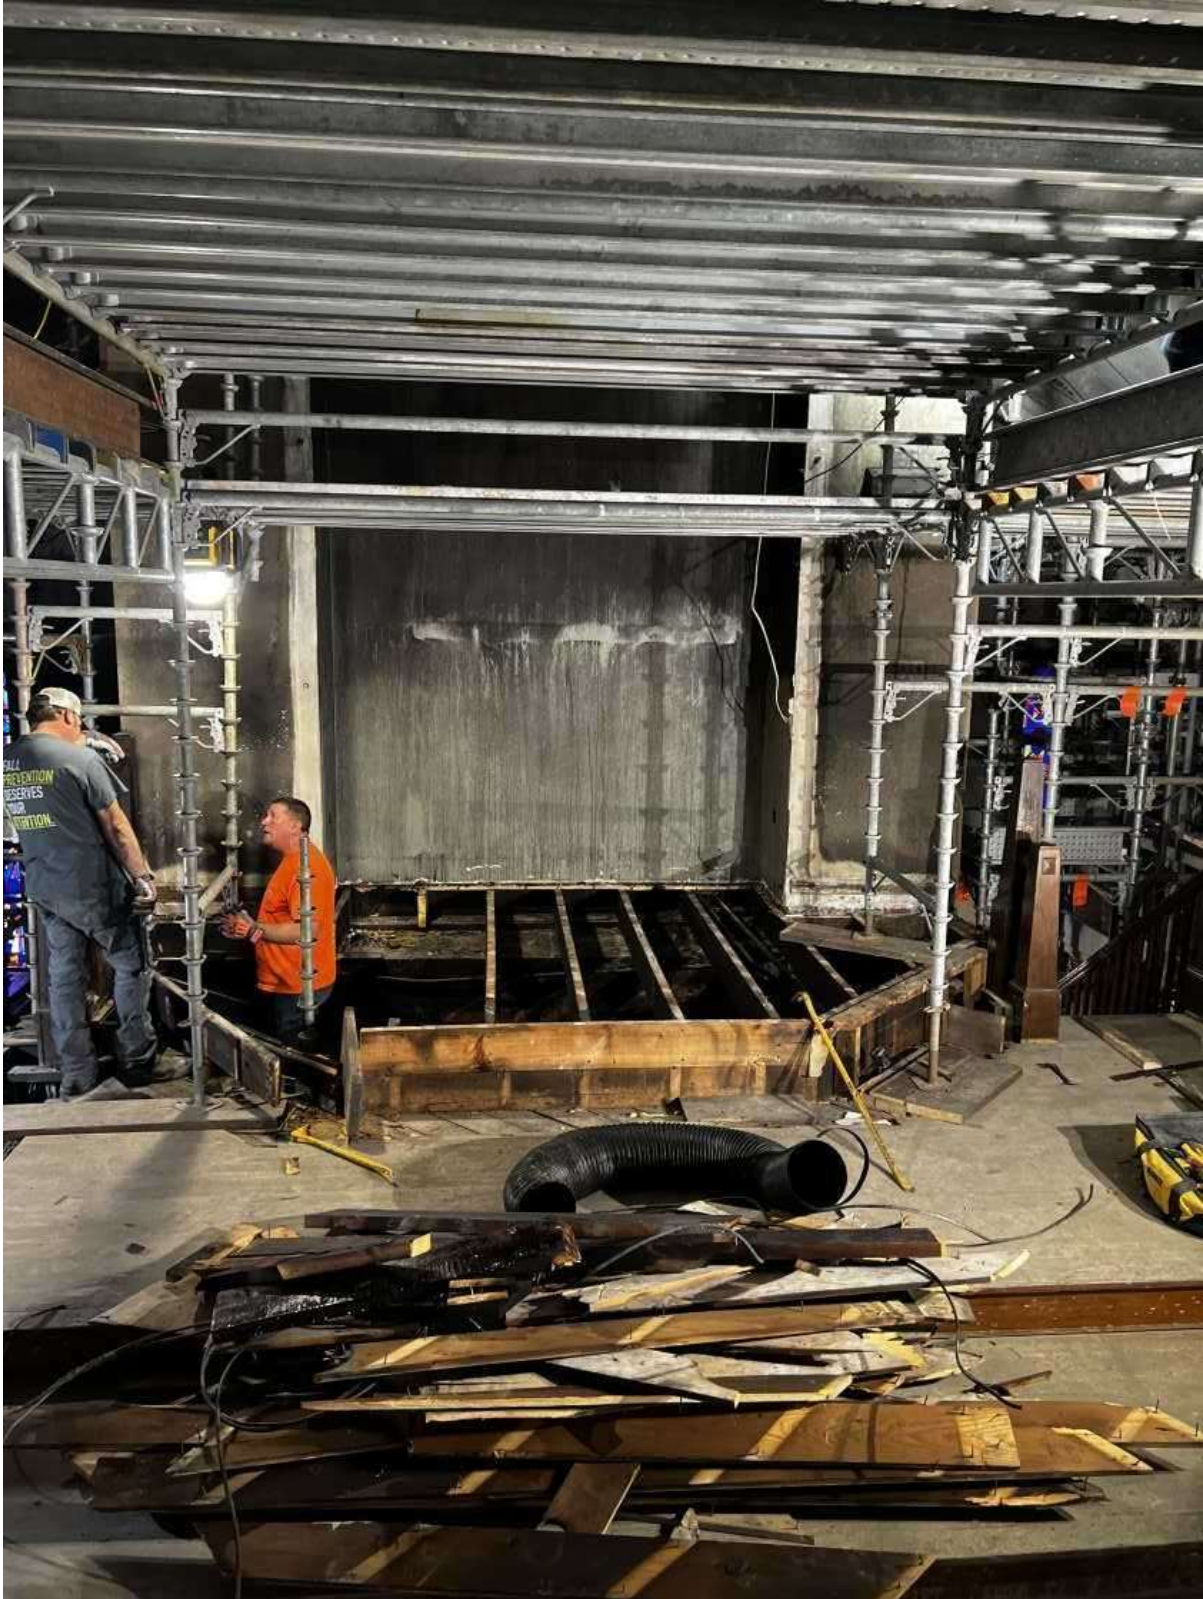

Where the organ pipes and risers were in the choir loft.

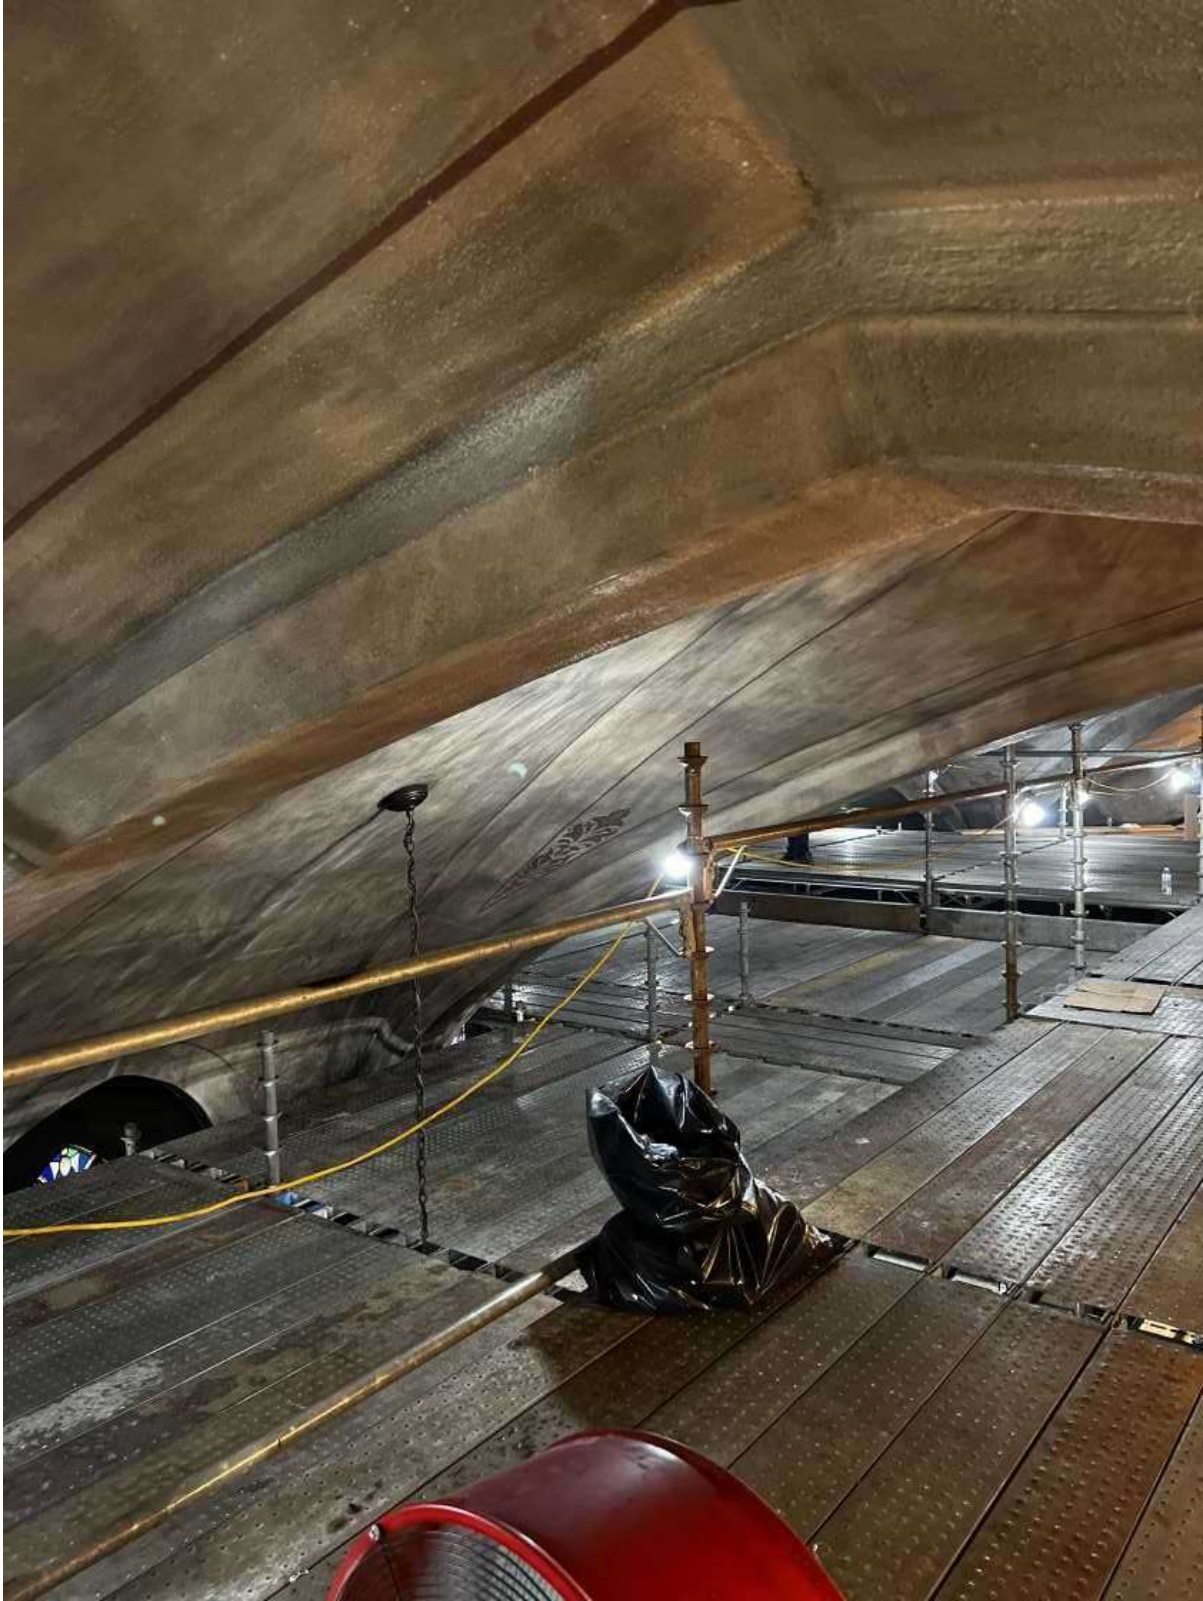

Ceiling before cleaning.



