

HOLY CROSS REBUILD UPDATES

DECEMBER 22, 2023



*Prepping for bathroom addition.
This is the space under the west choir steps.*



Framing the new bathroom space.



Picture 1: Obsolete boiler in west church basement space.



Picture 2: Same space after boiler removal.


JANUARY 13, 2024

*Pictures of the New
North/Gathering Space Wall*



JANUARY 28, 2024

*Mechanical Room added above the new bathroom
for furnaces, electrical boxes, and extra storage.*

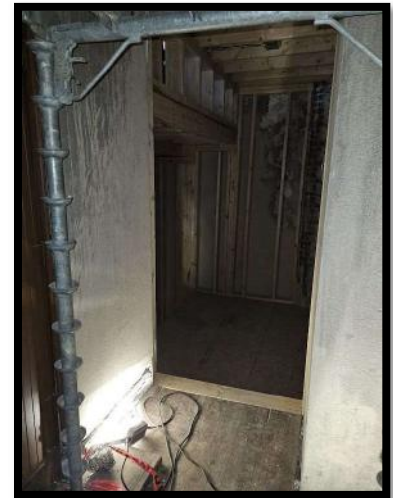

Picture 1: View at the Bell Rope level facing West.

Picture 2: View standing just inside the door.

Room is two-levels to accommodate the airflow



HOLY CROSS REBUILD UPDATES

FEBRUARY 4, 2024

Painters will apply a base coat of paint this week. All other contractors have been asked to pause their work. Due to miscommunication or misunderstanding, we now realize that not all windows will be removed for restoration. Just six windows, in the North half of the Church will be taken off site.



Picture 1: Choir loft Northwest Corner (West Stairs Removed)

Picture 2: Choir loft from the middle of the loft (looking North)

Picture 3: Base/sealer paint on the East wall (no more smoke and water)

Picture 4: Covering the holes in the wall where registers used to be.

FEBRUARY 19, 2024

Picture depicts utilizing the design from the top of our stained-glass windows to create the design for the choir loft rail. This sample design is not exact (but close), is approximately 40" tall, and there will be 12 panels like this across the span of the rail.



HOLY CROSS REBUILD UPDATES

FEBRUARY 15, 2024


Reredos Work in Progress

More Beautiful than Before! Some of the pieces are already loaded in the trailer and ready to come home.



HOLY CROSS REBUILD UPDATES

FEBRUARY 22, 2024

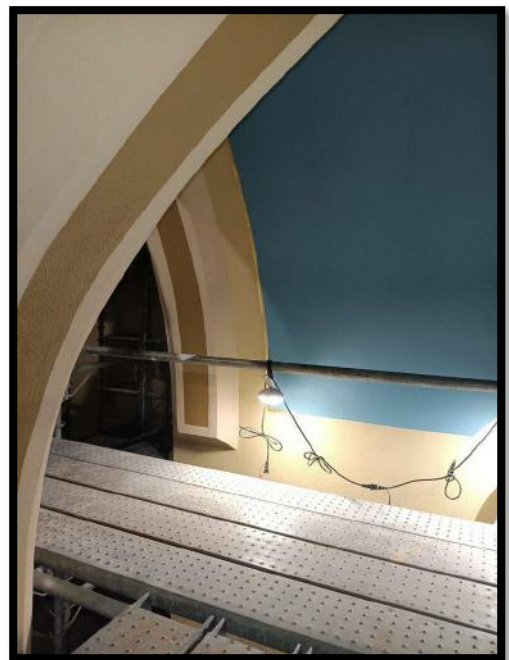

HOLY CROSS REBUILD UPDATES

FEBRUARY 22, 2024

